

**Final Project Completion Report**

**Project Name and Number:** Terminal Reservoir Basins I and II Joints Repairs, #4211

**Description:** The project includes the removal of existing joint material and installation of new joint materials in the interior of the Terminal Reservoir Basins I and II.

**District Project Manager:** Marcelo Anglade


|                                       |             |                            |
|---------------------------------------|-------------|----------------------------|
| <b>Engineer:</b>                      | <b>JWCD</b> | <b>Design Status: 100%</b> |
| Original Engineering Contract Amount: |             | N/A                        |
| Current Engineering Contract Amount:  |             | N/A                        |

|   |                             |                                  |
|---|-----------------------------|----------------------------------|
| <b>Contractor:</b>  | <b>TJ Lotz Construction</b> | <b>Construction Status: 100%</b> |
| Original construction contract amount:                    |                             | \$93,093                         |
| Total Change Order amount:                                |                             | \$0                              |
| Final construction contract amount:                       |                             | \$93,093                         |
| Total change orders as a percentage of original contract: |                             | 0.0%                             |
| Completion Schedule:                                      |                             |                                  |
|   | Notice to Proceed:          | 3/1/2021                         |
|   | Final Completion:           | 5/3/2021                         |

| <b>Summary of Change Orders:</b> |                            |               |
|----------------------------------|----------------------------|---------------|
|                                  | <b>Description</b>         | <b>Amount</b> |
|                                  |                            |               |
|                                  |                            |               |
|                                  |                            |               |
|                                  | Total Change Order Amount: | \$0           |



**Final Project Completion Report**

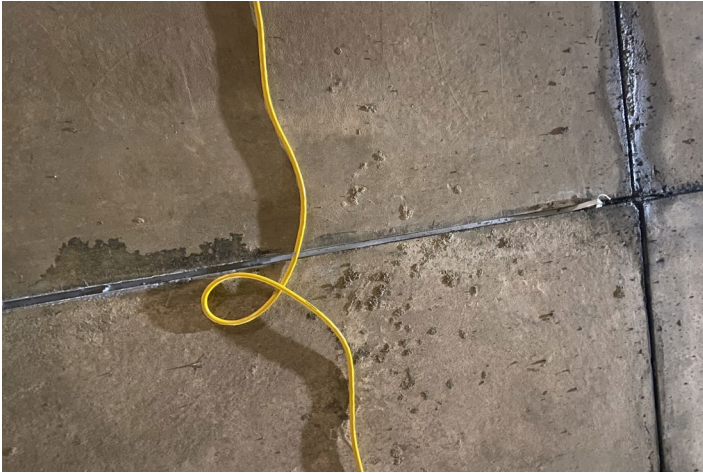

Preparing to install backing tape and primer.



Sikagard-62 primer placed in preparation for joint sealant.



Installation of the backing tape and Sikagard-62 primer.



Installation of Sikaflex joint sealant on floor.
