

Final Project Completion Report

Project Name and Number: 11400 South Redwood Road Meter Vault Rehabilitation, #4283

Description: The meter station serving South Jordan City at the corner of 11400 South and Redwood Road was constructed in 1982 and experienced corrosion and age-related wear. This project rehabilitated the meter vault to ensure its continued reliable operation. The project included replacing the main piping and related equipment, improving vault ventilation, and sealing the vault access to provide additional protection to the vault in the future. Cost was shared between JWCD and the City by a Cost Sharing Agreement.

District Project Manager: Conor Tyson

Engineer: JWCD Staff	Design Status: 100%
Original Engineering Contract Amount:	N/A
Final Engineering Contract Amount:	N/A

Contractor: Corrio Construction	Construction Status: 100%
Original construction contract amount:	\$91,561
Total Change Order amount:	\$477
Final construction contract amount:	\$92,038
Total change orders as a percentage of original contract:	0.5%
Completion Schedule:	
Notice to Proceed:	11/22/2022
Final Completion:	4/7/2023

Summary of Change Orders:		Amount
	Description	
1	Replace ventilation fan	\$477
Total Change Order Amount:		\$477

Final Project Completion Report



Removing the old corroded pipe




Installing new pipe in vault



New installed ventilation fan



Sealing manhole to limit water intrusion

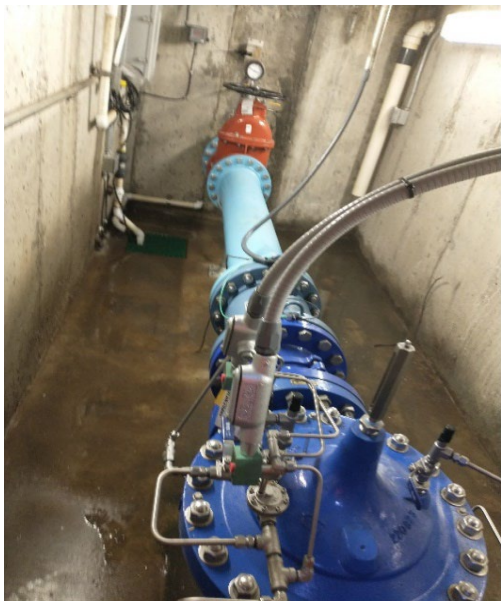

New pipeline, meter, and valves



New pipeline, meter, and valves
