

Final Project Completion Report

Project Name and Number: 9800 South 2300 East Well Re-Lining, #4119

Description: Installation of new 16-inch diameter stainless-steel screens and steel casing at the 9800 South 2300 East Well. The new screens were installed inside the existing 20-inch diameter screens which are deteriorating with age.

District Project Manager: Kevin Rubow

Engineer:	CRS Engineers	Design Status: 100%
Original Engineering Contract Amount:		\$15,380
Current Engineering Contract Amount:		\$15,380

Contractor:	Layne Christensen Company	Construction Status: 100%
Original construction contract amount:		\$128,555
Total Change Order amount:		\$32,665
Final construction contract amount:		\$161,220
Total change orders as a percentage of original contract:		25.4%
Completion Schedule:		
	Notice to Proceed:	7/28/2020
	Final Completion:	1/29/2021

Summary of Change Orders:		
	Description	Amount
1	Perform a 16" and 14" alignment test in the existing well casing.	\$29,265
2	Increased quantity of gravel pack for the 16" well liner.	\$10,900
3	Reconcile unused work and material quantities.	-\$7,500
	Total Change Order Amount:	\$32,665

Final Project Completion Report




Mobilizing to site to perform the alignment test.



Installation of the first section of the 16" stainless steel screens.



Welding of a steel casing joint.

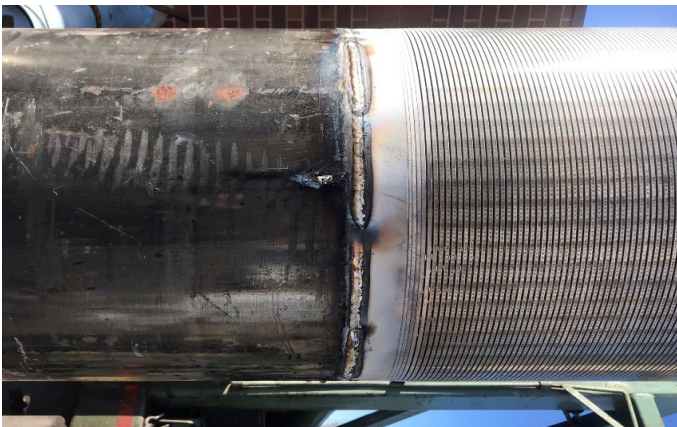

Welded joint, transitioning from stainless steel screens to steel casing.



Installation of the steel casing.
