

## Final Project Completion Report

**Project Name and Number:**        **Lower Campus Paving, #3910**

**Description:** Site drainage improvements and parking lot pavement for the Lower Campus.

**District Project Manager:** **Marcelo Anglade**

<b>Engineer:</b>	<b>Talisman Civil Consultants</b>	<b>Design Status: 100%</b>
Original Engineering Contract Amount:		\$289,917
Final Engineering Contract Amount:		\$319,427

<b>Contractor:</b>	<b>(Contractor's Name)</b>	<b>Construction Status: 100%</b>
Original construction contract amount:		\$1,444,512
Total Change Order amount:		
Final construction contract amount:		\$1,569,802
Total change orders as a percentage of original contract:		8.7%
Completion Schedule:		
Notice to Proceed:		7/27/2018
Final Completion:		1/17/2020

<b>Summary of Change Orders:</b>		
	<b>Description</b>	<b>Amount</b>
1	Potholing to find a gas leak	\$2,745
2	Supply and installation of a new gas line	\$44,275
3	Modify 10-inch water line to loop under new storm drain pipe	\$8,460
4	Supply and install geo textile fabric on excavated subgrade	\$26,991
5	Additional potholing and excavation and credits for storage bins	-\$483
6	Additional excavation, concrete and asphalt work	\$31,713
7	Additional base course and concrete cement	\$11,590
	Total Change Order Amount:	\$125,290


## Final Project Completion Report




New Asphalt at North Gate



Looking west towards North Canal Bridge

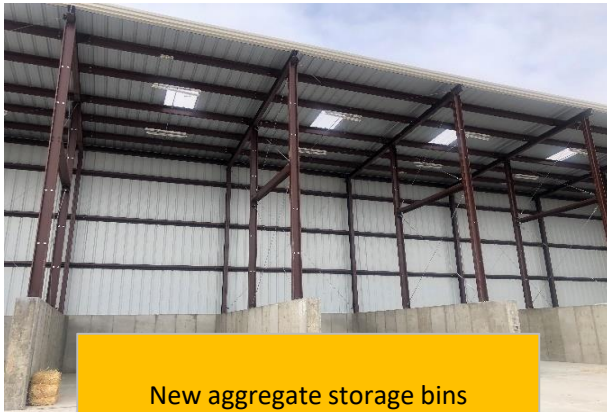

New aggregate storage bins

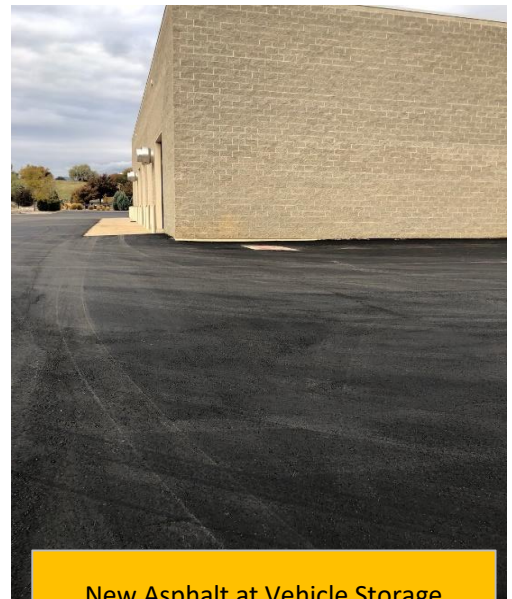

New Asphalt at Vehicle Storage Building
