

Final Project Completion Report

Project Name and Number: Midvale Retail Transfer, #4133

Description: Midvale City administered a construction project to connect the District's 1000 East retail system to Midvale's water system and transfer over 500 retail accounts. As part of the retail transfer project, Midvale's construction contractor made additional improvements to the District's transmission system. The City managed and paid for this project, and the District reimbursed applicable expenses, in accordance with a cost sharing agreement.

District Project Manager: Kevin Rubow

Engineer:	Hansen Allen and Luce (Midvale City)	Design Status: 100%
Original Engineering Contract Amount:		By Midvale City
Final Engineering Contract Amount:		By Midvale City

Contractor:	Noland & Son Construction (Midvale City)	Construction Status: 100%
Original construction contract amount:		\$108,160
Total Change Order amount:		\$28,300
Final construction contract amount:		\$136,460
Total change orders as a percentage of original contract:		26.2%
Completion Schedule:		
Notice to Proceed:		6/2/2019
Final Completion:		6/25/2020

Summary of Change Orders:		
	Description	Amount
1	Add a fire hydrant and service connection at 1223 East 7800 South.	\$23,910
2	Abandonment at 7575 South Union Park Avenue.	\$4,390
	Total Change Order Amount:	\$28,300


Final Project Completion Report



Night time water shutdown to minimize customer impact.



Coating existing turnout on the 900 East pipeline.

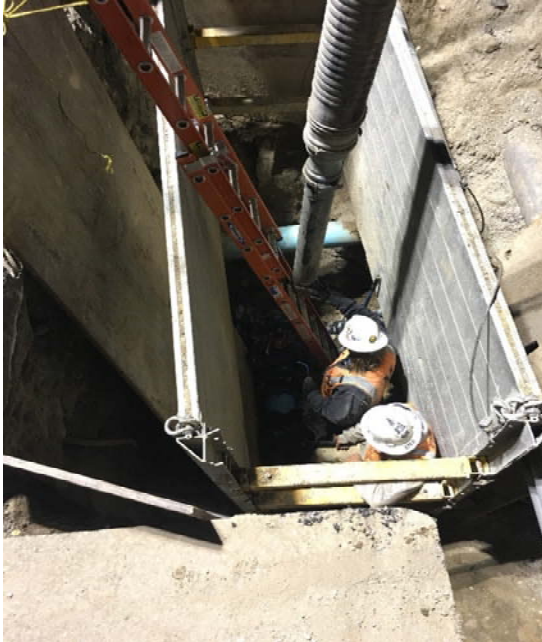

Connecting Fort Union shopping center to Midvale's water system.



Performing valve abandonment on Union Park Avenue.
