

**Final Project Completion Report**

**Project Name and Number:** 11800 S Zone C Pump Station, #4068

**Description:** Upgrade existing pump station to add 900 HP pump and variable speed drive


**District Project Manager:** Don Olsen/David McLean

<b>Engineer:</b>	<b>JVWCD Staff</b>	<b>Design Status: 100%</b>
Original Engineering Contract Amount:	Not Applicable	
Final Engineering Contract Amount:	Not Applicable	

<b>Contractor:</b>	<b>Corrio Construction</b>	<b>Construction Status: 100%</b>
Original construction contract amount:		\$572,416
Total Change Order amount:		-\$10,433
Final construction contract amount:		\$561,983
Total change orders as a percentage of original contract:		-1.8%
Completion Schedule:		
Notice to Proceed:		7/9/2018
Final Completion:		5/15/2019

<b>Summary of Change Orders:</b>		
	<b>Description</b>	<b>Amount</b>
1	Provide Victaulic Couplings in Lieu of Depend - O - Lock Couplings	-\$10,433
	Total Change Order Amount:	-\$10,433

Final Project Completion Report

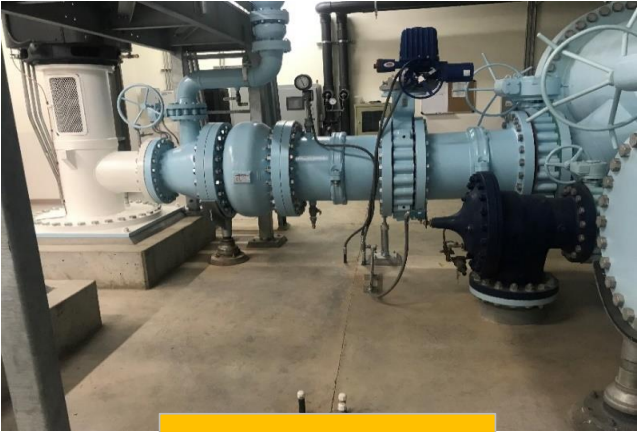

Completed piping



Construction in progress



Installation of new pump



Installed pump and motor
