

**Final Project Completion Report**

**Project Name and Number:** 9800 S 2300 E Well Development and Pump Testing, #4119

**Description:** Well development and pump testing to determine the capacity of the 9800 South 2300 East well. Following the well lining project, pump testing was required to determine the capacity of the well. The data collected from the pump testing will be used to specify the new pumping equipment and installed under a separate contract.

**District Project Manager:** Kevin Rubow

<b>Engineer:</b>	<b>CRS Engineers</b>	<b>Design Status: 100%</b>
Original Engineering Contract Amount:	(Included as an amendment to the Four Well Project)	
Engineering Expenditures for this Project:	\$4,350	

<b>Contractor:</b>	<b>Boart Longyear Company</b>	<b>Construction Status: 100%</b>
Original construction contract amount:	\$65,880	
Total Change Order amount:	\$1,680	
Final construction contract amount:	\$67,560	
Total change orders as a percentage of original contract:	2.6%	
Completion Schedule:		
Award of Purchase Order:	3/25/2021	
Final Completion:	6/15/2021	

<b>Summary of Change Orders:</b>		
	<b>Description</b>	<b>Amount</b>
	1 Additional pump testing hours.	\$1,680
	Total Change Order Amount:	\$1,680



## Final Project Completion Report




Generator and pump discharge head.



Installation of the test pumping equipment.



Sound attenuation panels.

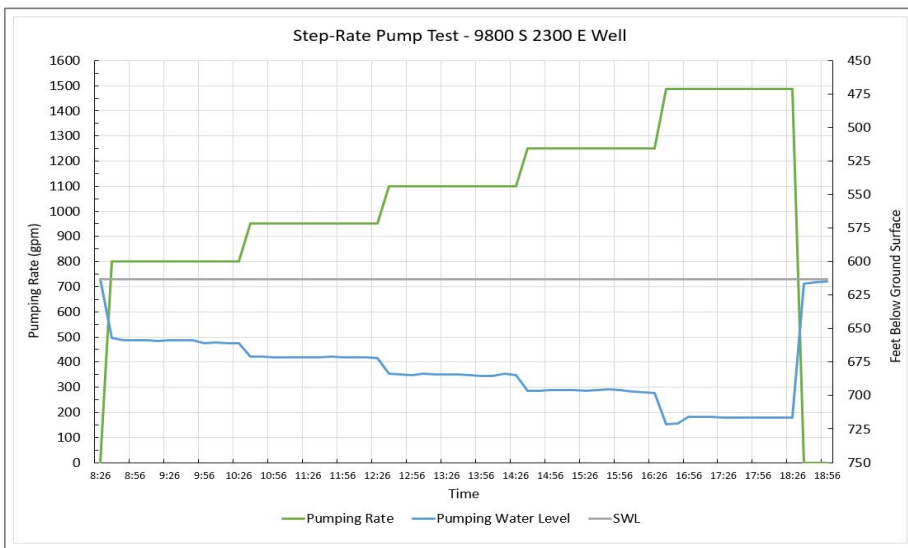

Pumping drawdown and flow rate data.
