

Final Project Completion Report

Project Name and Number: Cost Sharing of 7271 West 11800 South Pipeline Extension, 3978

Description: The project supported the construction of a dual-pressure zone meter station for Herriman City. Cost sharing was necessary because of the District's future plans to co-locate a pump station on-site. Although the City only required a 18" diameter pipeline, the District required a 48" diameter pipeline for its future pump station. This project installed all of the necessary improvements. The City managed and paid for this project. The District reimbursed applicable expenses.


District Project Manager: David McLean

Engineer:	Hansen Allen and Luce (via cost sharing agreement with Herriman City)	Design Status: 100%
Original Engineering Contract Amount:		\$28,500
Final Engineering Contract Amount:		\$32,475

Contractor:	VanCon, Inc. (via cost sharing agreement with Herriman City)	Construction Status: 100%
Original construction contract amount:		\$248,612
Total Change Order amount:		\$18,780
Final construction contract amount:		\$267,392
Total change orders as a percentage of original contract:		7.6%
Completion Schedule:		
Notice to Proceed:		2/1/2019
Final Completion:		10/15/2019

Summary of Change Orders:		
	Description	Amount
1	Flowable Fill pipe bedding to match District standards	\$15,622
2	Additional rip-rap armoring for site stormwater control	\$3,158
	Total Change Order Amount:	\$18,780

Final Project Completion Report

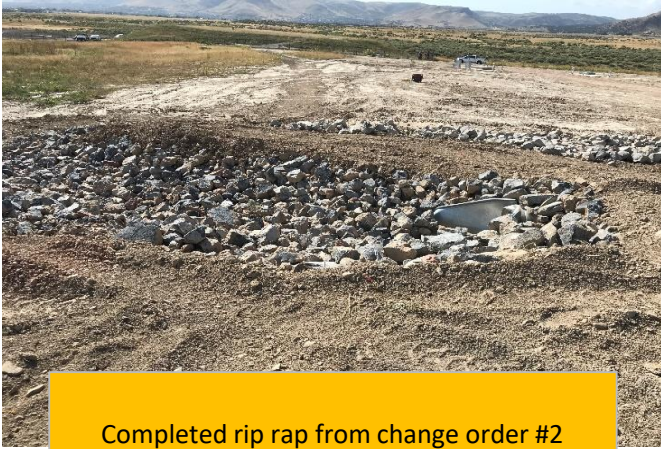

Completed rip rap from change order #2



Completed meter station from exterior



Completed pipeline awaiting backfill



Turn-out vault construction



Pipeline material ready for installation



Completed meter station from interior
