

Final Project Completion Report

Project Name and Number: 3200 West 6200 South Vault Upgrades, #4111

Description: Refurbishment of an existing valve vault located at 3200 West 6200 South on the 33-inch cross valley pipeline. The improvements included replacement of corroded piping and valves, installation of passive air venting and access ladder, and application of paint coatings.

District Project Manager: Kevin Rubow

Engineer:	JVWCD Staff	Design Status: 100%
Original Engineering Contract Amount:	Not applicable	
Final Engineering Contract Amount:	Not applicable	

Contractor:	Inc.	Construction Status: 100%
Original construction contract amount:		\$83,770
Total Change Order amount:		\$15,875
Final construction contract amount:		\$99,645
Total change orders as a percentage of original contract:		19.0%
Completion Schedule:		
	Notice to Proceed:	2/27/2019
	Final Completion:	1/3/2020


Summary of Change Orders:		
	Description	Amount
1	Installation of passive air vent system.	\$9,600
2	Installation of vault equipment access lid.	\$3,950
3	Contract extension/remobilization due to JVWCD shutdown issues.	\$2,325
	Total Change Order Amount:	\$15,875




Final Project Completion Report



Removal of existing 12" valve

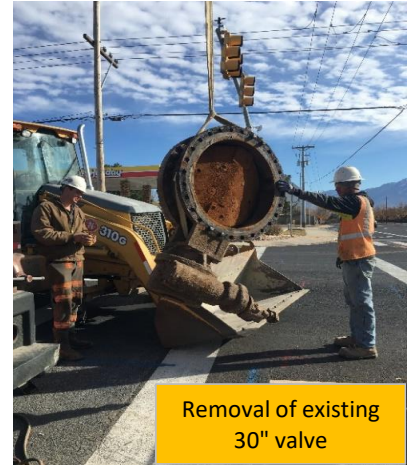


Removal of existing 30" valve

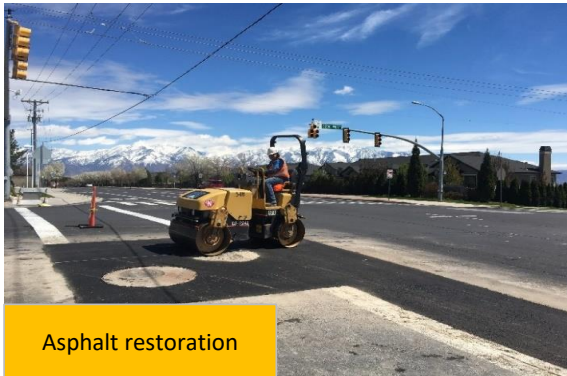

Asphalt restoration



Passive air venting for vault

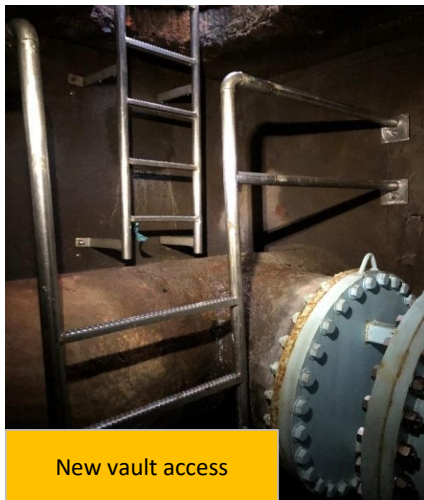

New vault access



12" valve and piping
