

Final Project Completion Report

Project Name and Number: Headquarters and JWTP HVAC Integration, #3967

Description: This project included combining the Building Automation Systems at the JWTP and Administration Buildings with the objective of allowing Maintenance Department personnel to monitor and control the HVAC equipment, temperature, etc. at the both these locations. This entailed the installation of hardware to permit connectivity between the existing HVAC equipment and computers at the Maintenance Building.

District Project Manager:

Engineer:	Alliance Energy & Integration	Design Status: 100%
Original Engineering Contract Amount:		\$35,600
Final Engineering Contract Amount:		\$35,600

Contractor:	Alliance Energy & Integration	Construction Status: 100%
Original const. contract amount: (Alliance was the designer and contractor)		\$35,600
Total Change Order amount:		\$0
Final construction contract amount:		\$35,600
Total change orders as a percentage of original contract:		0.0%
Completion Schedule:		
Notice to Proceed:		10/31/2018
Final Completion:		9/1/2020


Final Project Completion Report



Equipment controlled by the new integration program (Typ.)



Hardware connecting equipment to network.

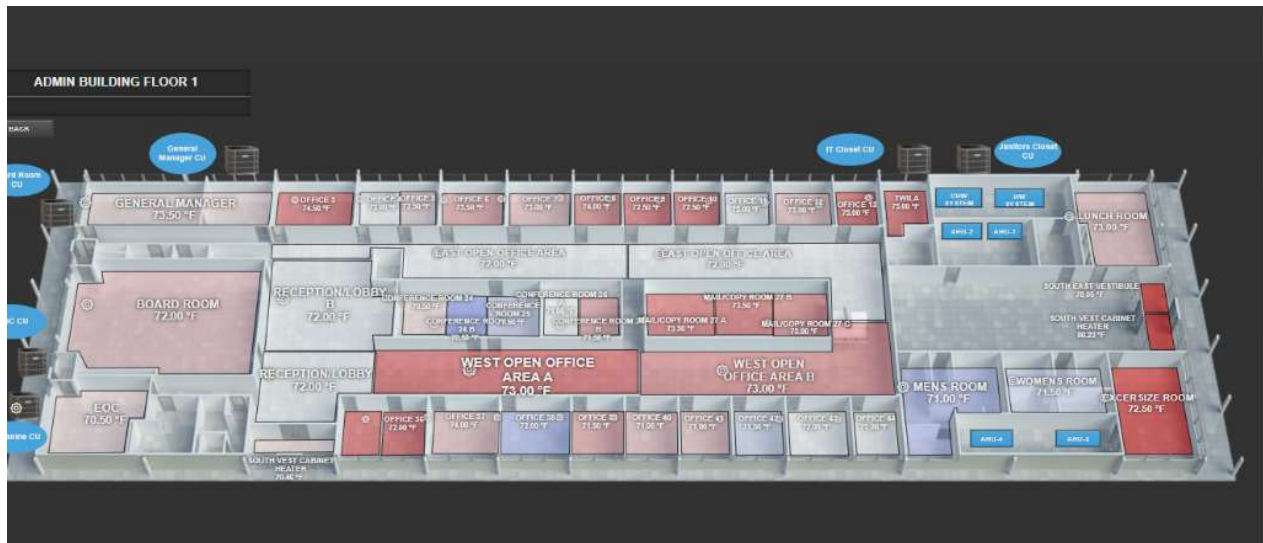

Computer Interface - Operator's computer screen
