

## Final Project Completion Report

**Project Name and Number:**

**7618 S. 700 E. Well Storm Drain, 3906**

**Description:** The 7618 S. 700 E. well storm drain connects stormwater from the 7618 S. 700 E. well site to the Sandy City storm drain network . The storm drain allows the stormwater runoff collected from the well to be discharged off site.

<b>Engineer: Horrock Engineers</b>	<b>Design Status: 100%</b>
Original Engineering Contract Amount:	\$5,000

<b>Contractor: Lyndon Jones Construction</b>	<b>Construction Status: 100%</b>
Original construction contract amount:	\$59,153
Total Change Order amount:	-\$839
Final construction contract amount:	\$58,314
Total change orders as a percentage of original contract:	-1.4%

<b>Summary of Change Orders:</b>	
Description	Amount
1 Remove concrete pad from scope of work	-\$2,208
2 Loop of underground television transmission cable	\$1,369
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	

**TOTAL CHANGE ORDER AMOUNT:** -\$839.00




Construction on Woodpine Circle, Sandy, Utah



Completed work



Construction at Briarwood Condominiums

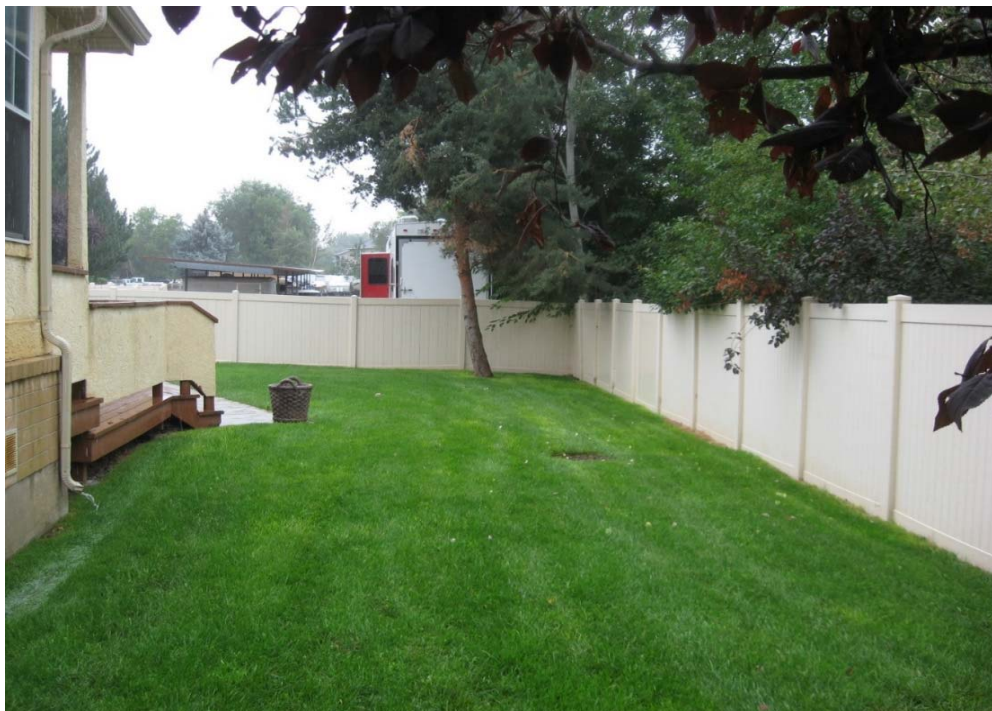

Completed work





Construction connecting in to existing upstream storm drain system



Completed work
