

Final Project Completion Report

Project Name and Number: SERWTP Filter Bldg Improvements-Roof Replacement, #3944

Description: Demolition and removal of existing tile roofing on the Filter Building and re-roofing with 50-year warranty roof shingles. Also, installation of Thermoplastic Polyolefin roofing membrane on the Filter Building Clerestory, Reclaim Water Pump Building roof, and the Actiflo Clerestory.

Engineer:	JVWCD staff	Design Status: 100%
Current Contract Amount		

Summary of Design Amendments:		
	Description	Amount
1	None	n/a
Total Design Change Order Amount:		\$0


Contractor:	Contract West Roofing, Inc.	Construction Status: 100%
Original construction contract amount:		\$63,300
Total Change Order amount:		\$2,440
Current construction contract amount:		\$65,740
Total change orders as a percentage of original contract:		3.9%

Summary of Construction Change Orders:		
	Description	Amount
1	Install Thermoplastic Polyolefin on Actiflo Building Clerestory	\$2,440
Total Construction Change Order Amount:		\$2,440

Final Project Completion Report



Filter Building south view

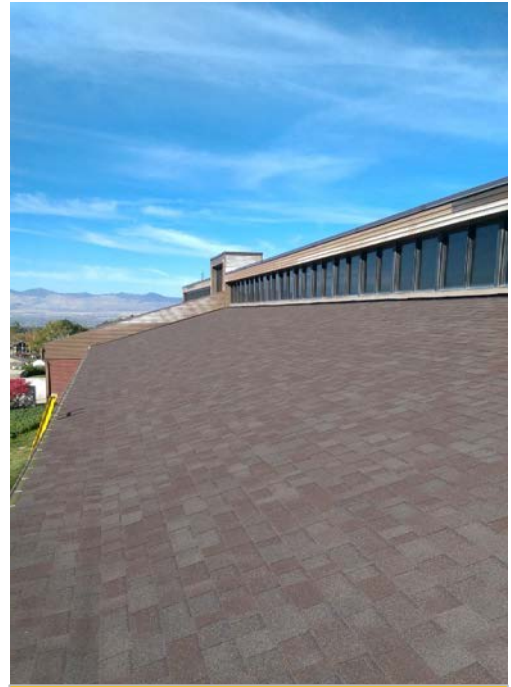

New architectural shingle



Filter Building Clerestory
Thermoplastic Polyolefin



Reclaim Water Pump Building new
Thermoplastic Polyolefin roofing
