

Final Project Completion Report

Project Name and Number: **10200 South Bangerter Highway Casing, #4188**

Description: The Utah Department of Transportation (UDOT) has awarded a contract to construct three grade separated interchanges along Bangerter Highway at 12600 South, 10400 South, and 6200 South. During the review of the UDOT project design, District staff identified an opportunity to install a 60-inch casing for a future upgrade of the 10200 South Pipeline. A new 48-inch pipeline will be needed at this location by 2040. Installing a casing now preserves a corridor for the future 48-inch pipeline and significantly reduces future construction costs.

District Project Manager: **Travis Christensen**

Engineer: Bowen Collins & Associates	Design Status: 100%
Original Engineering Contract Amount:	\$24,390
Final Engineering Contract Amount:	\$43,231

Contractor: UDOT (WW Clyde/RL Wadsworth)	Construction Status: 100%
Original construction contract amount:	\$230,434
Total Change Order amount:	\$0
Final construction contract amount:	\$230,434
Total change orders as a percentage of original contract:	0.0%
Completion Schedule:	
Notice to Proceed:	6/1/2020
Final Completion:	2/1/2022

Summary of Change Orders:		
	Description	Amount
	Total Change Order Amount:	\$0

Final Project Completion Report




Dec 3, 2021 at 8:26:04 AM
 Bangerter Hwy
 South Jordan, UT 84095
 United States



Installation of the 60" casing through the JA-2 easement

60" casing prior to installation

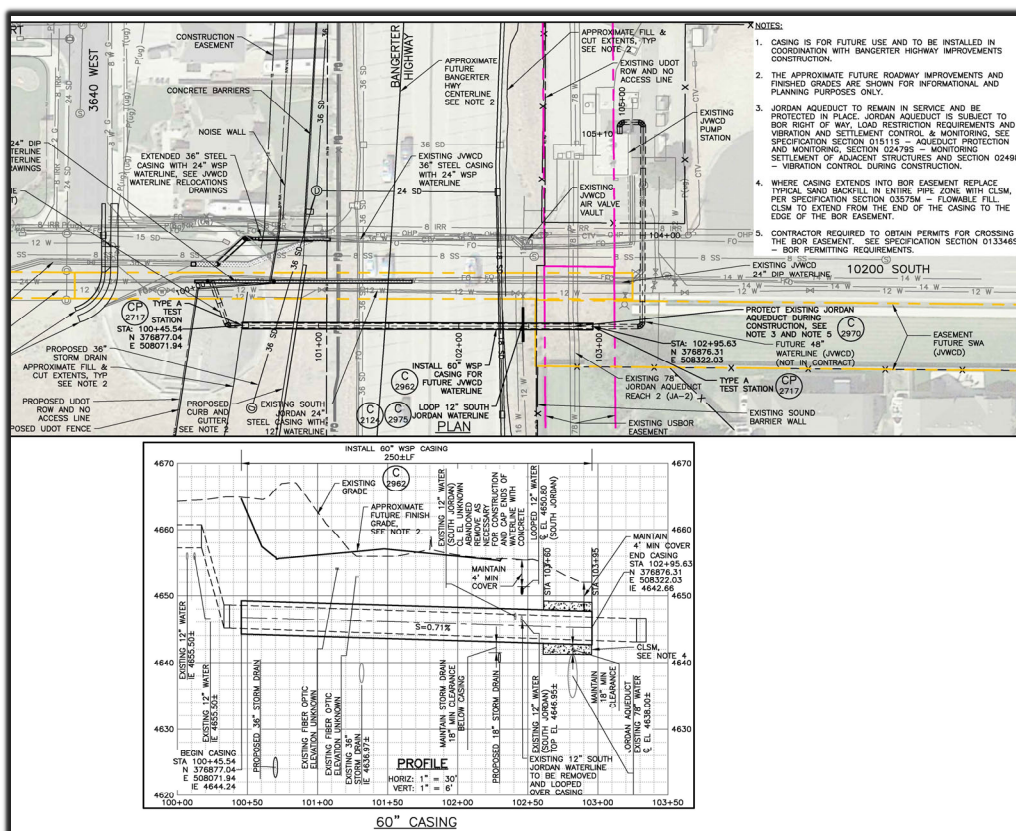

Plan sheet from the 60" casing crossing Bangerter Highway
